Dataforensics

Borehole ID: BH-33

Client: Geo-Institute
Project Name: Vendor DIGGS Challenge
Project Number: 20250110 - DIGGS Challenge
Project Location: Somewhere Over the Rainbow
Date Started: Jun 04 2015 **Completed:** Jun 04 2015
Logged By: Scott Deaton **Checked By:**
Drilling Contractor: Big Dog Drillers
Northing: 1402115.2 **Easting:** 2272085.8 **Elevation:** 318.00
Drilling Method: 4.25" Hollow stem auger, NQ
Ground Water Levels
Equipment: CME 550, Arco 9000
At time of drilling 15.00 on Jun 04 2015
Hammer Type: Automatic
End of drilling 13.00 on Jun 04 2015
Notes: Notes go here
After drilling 15.00 on Jun 05 2015

Depth (ft)	Graphic	Material Description	Elevation (ft)	Sample Type	Number	Recovery %	Blow Counts (N Value)	Pocket Pen. (tsf)	Dry Unit Wt. (pcf)	SPT N Value / MC (%) / PL & LL (%) / Fines Content (%) (20 40 60 80)
		Asphalt								
1		POORLY GRADED GRAVEL WITH CLAY AND SAND (GP-GC); mostly fine to medium very hard subrounded flat GRAVEL; some fine hard well rounded elongated sand; few low plasticity fines; dark brownish black and light grayish brown, moist to wet, medium dense, stratified, trace ferrous nodules, trace construction debris, trace manganese, no odor, moderate cementation, iron oxide staining, max size = 3 in., Something else goes here, FILL Unit A								
2					1				100	
3										
4										
5			313.0							
6		LEAN CLAY (CL); mostly low plasticity FINES no dilatancy; dark brown, moist, medium stiff to stiff, varved, FILL Unit A								
7								0.25		
8					2	100	1-2-1 (3)			
9										
10			308.0					2.25		
11		POORLY GRADED SAND (SP); mostly rounded SAND; light brown, moist, loose to medium dense, trace silt, hydrocarbon odor, ALLUVIUM Unit A			3A 3B	93	2-4-6 (10)			
12										
13					4	87	3-6-9 (15)			
14										
15			303.0							
16					5	67	5-10-15 (25)			
17		LEAN CLAY (CL); mostly medium plasticity FINES; dark brown, moist to wet, very stiff to very hard, iron oxide staining, ALLUVIUM Unit A						3.50		

Dataforensics

Borehole ID: BH-33

Client: Geo-Institute
Project Name: Vendor DIGGS Challenge
Project Number: 20250110 - DIGGS Challenge
Project Location: Somewhere Over the Rainbow
Date Started: Jun 04 2015 **Completed:** Jun 04 2015
Logged By: Scott Deaton **Checked By:**
Drilling Contractor: Big Dog Drillers
Northing: 1402115.2 **Easting:** 2272085.8 **Elevation:** 318.00
Drilling Method: 4.25" Hollow stem auger, NQ
Ground Water Levels
Equipment: CME 550, Arco 9000
At time of drilling 15.00 on Jun 04 2015
Hammer Type: Automatic
End of drilling 13.00 on Jun 04 2015
Notes: Notes go here
After drilling 15.00 on Jun 05 2015

Depth (ft)	Graphic	Material Description	Elevation (ft)	Sample Type	Number	Recovery %	Blow Counts (N Value)	Pocket Pen. (tsf)	Dry Unit Wt. (pcf)
19		LEAN CLAY (CL); mostly medium plasticity FINES; dark brown, moist to wet, very stiff to very hard, iron oxide staining, ALLUVIUM Unit A			6	60	1-0-0 (WOH)		
20		becoming gray	298.0						
22								2.50	
23					7	100			
24								1.50	
25		FAT CLAY (CH); mostly high plasticity FINES; few fine sand; dark red, very dense, ALLUVIUM Unit B	293.0		8A 8B	83	9-12-50/2" (50/2")		
26		becoming wet							
27					9	71	15-50/2" (50/2")	4.50	
28					10	100	50/1" (50/1")	4.50	
30		CALCAREOUS LIMESTONE AND SANDSTONE, moderately weathered to highly weathered, dark brownish gray and light olive green, very fine grained to medium grained sand, strong to very strong, medium, 0° to 15° bedding angle, wet	288.0		R-1A				
32						100			
33		becoming vuggy			R-1B				
34		LIMESTONE, freshly weathered, dark gray, wet, Comments go here							
35			283.0						

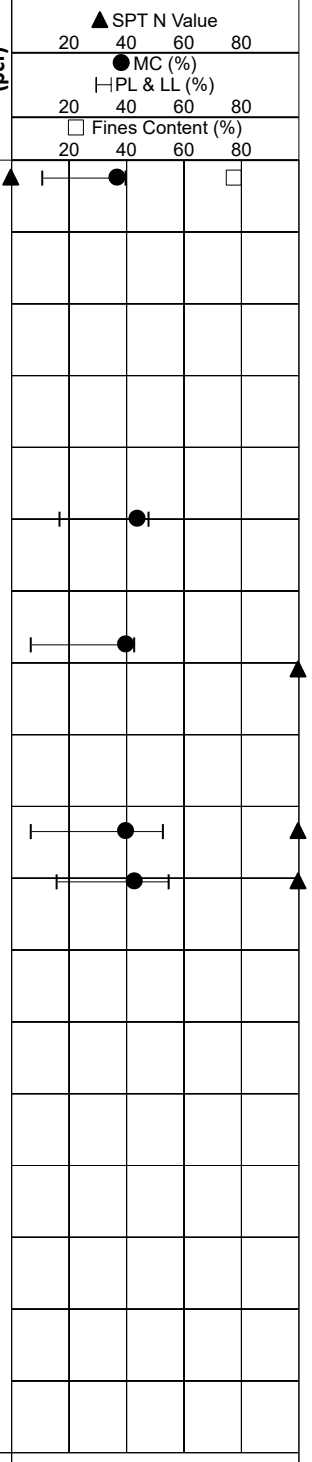

Dataforensics

Borehole ID: BH-33

Client: Geo-Institute
Project Name: Vendor DIGGS Challenge
Project Number: 20250110 - DIGGS Challenge
Project Location: Somewhere Over the Rainbow
Date Started: Jun 04 2015 **Completed:** Jun 04 2015
Logged By: Scott Deaton **Checked By:**
Drilling Contractor: Big Dog Drillers
Northing: 1402115.2 **Easting:** 2272085.8 **Elevation:** 318.00
Drilling Method: 4.25" Hollow stem auger, NQ
Ground Water Levels
Equipment: CME 550, Arco 9000
At time of drilling 15.00 on Jun 04 2015
Hammer Type: Automatic
End of drilling 13.00 on Jun 04 2015
Notes: Notes go here
After drilling 15.00 on Jun 05 2015

Depth (ft)	Graphic	Material Description	Elevation (ft)	Sample Type	Number	Recovery %	Blow Counts (N Value)	Pocket Pen. (tsf)	Dry Unit Wt. (pcf)	▲ SPT N Value 20 40 60 80 / ● MC (%) ⊢PL & LL (%) 20 40 60 80 / ☐ Fines Content (%) 20 40 60 80
		LIMESTONE, freshly weathered, dark gray, wet, Comments go here			R-2	80				
37										
38										
39										
40		Boring terminated at 40.0 feet.	278.0							
41										
42										
43										
44										
45			273.0							
46										
47										
48										
49										
50			268.0							
51										
52										
53										

Dataforensics

Borehole ID: BH-33

Client: Geo-Institute
Project Name: Vendor DIGGS Challenge
Project Number: 20250110 - DIGGS Challenge
Project Location: Somewhere Over the Rainbow
Date Started: Jun 04 2015 **Completed:** Jun 04 2015
Logged By: Scott Deaton **Checked By:**
Drilling Contractor: Big Dog Drillers
Northing: 1402115.2 **Easting:** 2272085.8 **Elevation:** 318.00
Drilling Method: 4.25" Hollow stem auger, NQ
Ground Water Levels
Equipment: CME 550, Arco 9000
At time of drilling 15.00 on Jun 04 2015
Hammer Type: Automatic
End of drilling 13.00 on Jun 04 2015
Notes: Notes go here
After drilling 15.00 on Jun 05 2015

Depth (ft)	Graphic	Material Description	Elevation (ft)	Sample Type	Number	Recovery % RQD	Blow Counts (N Value)	Pocket Pen. (tsf)	Dry Unit Wt. (pcf)	Moisture Content	Atterberg Limits: Liquid Limit	Atterberg Limits: Plastic Limit	Atterberg Limits: Plasticity Index	Fines Content (%)
		Asphalt												
1		POORLY GRADED GRAVEL WITH CLAY AND SAND (GP-GC); mostly fine to medium very hard subrounded flat GRAVEL; some fine hard well rounded elongated sand; few low plasticity fines; dark brownish black and light grayish brown, moist to wet, medium dense, stratified, trace ferrous nodules, trace construction debris, trace manganese, no odor, moderate cementation, iron oxide staining, max size = 3 in., Something else goes here, FILL Unit A												
2					1				100	32				5
3														
4														
5			313.0											
6		LEAN CLAY (CL); mostly low plasticity FINES no dilatancy; dark brown, moist, medium stiff to stiff, varved, FILL Unit A												
7								0.25						
8					2	100	1-2-1 (3)			33	41	11	30	
9														
10			308.0					2.25						
11		POORLY GRADED SAND (SP); mostly rounded SAND; light brown, moist, loose to medium dense, trace silt, hydrocarbon odor, ALLUVIUM Unit A			3A 3B	93	2-4-6 (10)			35				92
12														
13					4	87	3-6-9 (15)			41				22
14														
15			303.0											
16					5	67	5-10-15 (25)			39				
17		LEAN CLAY (CL); mostly medium plasticity FINES; dark brown, moist to wet, very stiff to very hard, iron oxide staining, ALLUVIUM Unit A						3.50						

Dataforensics

Borehole ID: BH-33

Client: Geo-Institute
Project Name: Vendor DIGGS Challenge
Project Number: 20250110 - DIGGS Challenge
Project Location: Somewhere Over the Rainbow
Date Started: Jun 04 2015 **Completed:** Jun 04 2015
Logged By: Scott Deaton **Checked By:**
Drilling Contractor: Big Dog Drillers
Northing: 1402115.2 **Easting:** 2272085.8 **Elevation:** 318.00
Drilling Method: 4.25" Hollow stem auger, NQ
Ground Water Levels
Equipment: CME 550, Arco 9000
At time of drilling 15.00 on Jun 04 2015
Hammer Type: Automatic
End of drilling 13.00 on Jun 04 2015
Notes: Notes go here
After drilling 15.00 on Jun 05 2015

Depth (ft)	Graphic	Material Description	Elevation (ft)	Sample Type	Number	Recovery % RQD	Blow Counts (N Value)	Pocket Pen. (tsf)	Dry Unit Wt. (pcf)	Moisture Content	Atterberg Limits: Liquid Limit	Atterberg Limits: Plastic Limit	Atterberg Limits: Plasticity Index	Fines Content (%)
19		LEAN CLAY (CL); mostly medium plasticity FINES; dark brown, moist to wet, very stiff to very hard, iron oxide staining, ALLUVIUM Unit A			6	60	1-0-0 (WOH)			37	48,40	11,7	37,33	78
20		becoming gray	298.0											
22								2.50						
23					7	100				44	48	17	31	
25			293.0		8A 8B	83	9-12-50/2" (50/2")	1.50		40	43	7	36	
26		FAT CLAY (CH); mostly high plasticity FINES; few fine sand; dark red, very dense, ALLUVIUM Unit B becoming wet												
27					9	71	15-50/2" (50/2")	4.50		40	53	7	46	
28					10	100	50/1" (50/1")	4.50		43	55	16	39	
30		CALCAREOUS LIMESTONE AND SANDSTONE, moderately weathered to highly weathered, dark brownish gray and light olive green, very fine grained to medium grained sand, strong to very strong, medium, 0° to 15° bedding angle, wet	288.0		R-1A									
33		becoming vuggy			R-1B	100 60								
34		LIMESTONE, freshly weathered, dark gray, wet, Comments go here												
35			283.0											

Dataforensics

Borehole ID: BH-33

Client: Geo-Institute
Project Name: Vendor DIGGS Challenge
Project Number: 20250110 - DIGGS Challenge
Project Location: Somewhere Over the Rainbow
Date Started: Jun 04 2015 **Completed:** Jun 04 2015
Logged By: Scott Deaton **Checked By:**
Drilling Contractor: Big Dog Drillers
Northing: 1402115.2 **Easting:** 2272085.8 **Elevation:** 318.00
Drilling Method: 4.25" Hollow stem auger, NQ
Ground Water Levels
Equipment: CME 550, Arco 9000
At time of drilling 15.00 on Jun 04 2015
Hammer Type: Automatic
End of drilling 13.00 on Jun 04 2015
Notes: Notes go here
After drilling 15.00 on Jun 05 2015

Depth (ft)	Graphic	Material Description	Elevation (ft)	Sample Type	Number	Recovery % RQD	Blow Counts (N Value)	Pocket Pen. (tsf)	Dry Unit Wt. (pcf)	Moisture Content	Atterberg Limits: Liquid Limit	Atterberg Limits: Plastic Limit	Atterberg Limits: Plasticity Index	Fines Content (%)
37		LIMESTONE, freshly weathered, dark gray, wet, Comments go here			R-2	80								
38						40								
39														
40		Boring terminated at 40.0 feet.	278.0											
41														
42														
43														
44														
45			273.0											
46														
47														
48														
49														
50			268.0											
51														
52														
53														

Dataforensics

Borehole ID: BH-33

Client: Geo-Institute
Project Name: Vendor DIGGS Challenge
Project Number: 20250110 - DIGGS Challenge
Project Location: Somewhere Over the Rainbow
Date Started: Jun 04 2015 **Completed:** Jun 04 2015
Logged By: Scott Deaton **Checked By:**
Drilling Contractor: Big Dog Drillers
Northing: 1402115.2 **Easting:** 2272085.8 **Elevation:** 318.00
Drilling Method: 4.25" Hollow stem auger, NQ
Equipment: CME 550, Arco 9000
Hammer Type: Automatic
Notes: Notes go here

Ground Water Levels

At time of drilling	15.00 on Jun 04 2015
End of drilling	13.00 on Jun 04 2015
After drilling	15.00 on Jun 05 2015

Depth (ft)	Sample Type	Number	Blow Counts (N Value)	Environmental Data	Graphic	Material Description	Elevation (ft)	PID Concentration (125 250 375 500)	Well Details
						Asphalt			
1–3		1				POORLY GRADED GRAVEL WITH CLAY AND SAND (GP-GC); mostly fine to medium very hard subrounded flat GRAVEL; some fine hard well rounded elongated sand; few low plasticity fines; dark brownish black and light grayish brown, moist to wet, medium dense, stratified, trace ferrous nodules, trace construction debris, trace manganese, no odor, moderate cementation, iron oxide staining, max size = 3 in., Something else goes here, FILL Unit A			Concrete
4				PID = 100 PPM					
5							313.0		
7				PID = 200 PPM					
8–9		2	1-2-1 (3)			LEAN CLAY (CL); mostly low plasticity FINES no dilatancy; dark brown, moist, medium stiff to stiff, varved, FILL Unit A			Bentonite
10		3A	2-4-6 (10)	PID = 300 PPM			308.0		
11		3B				POORLY GRADED SAND (SP); mostly rounded SAND; light brown, moist, loose to medium dense, trace silt, hydrocarbon odor, ALLUVIUM Unit A			
12				PID = 400 PPM					
13–14		4	3-6-9 (15)						
15				PID = 500 PPM			303.0		
16		5	5-10-15 (25)			LEAN CLAY (CL); mostly medium plasticity FINES; dark brown, moist to wet, very stiff to very hard, iron oxide staining, ALLUVIUM Unit A			
17				PID = 600 PPM					

Dataforensics

Borehole ID: BH-33

Client: Geo-Institute
Project Name: Vendor DIGGS Challenge
Project Number: 20250110 - DIGGS Challenge
Project Location: Somewhere Over the Rainbow
Date Started: Jun 04 2015 **Completed:** Jun 04 2015
Logged By: Scott Deaton **Checked By:**
Drilling Contractor: Big Dog Drillers
Northing: 1402115.2 **Easting:** 2272085.8 **Elevation:** 318.00
Drilling Method: 4.25" Hollow stem auger, NQ
Equipment: CME 550, Arco 9000
Hammer Type: Automatic
Notes: Notes go here

Ground Water Levels
At time of drilling 15.00 on Jun 04 2015
End of drilling 13.00 on Jun 04 2015
After drilling 15.00 on Jun 05 2015

Depth (ft)	Sample Type	Number	Blow Counts (N Value)	Environmental Data	Graphic	Material Description	Elevation (ft)	PID Concentration (125 250 375 500)	Well Details
19		6	1-0-0 (WOH)			LEAN CLAY (CL); mostly medium plasticity FINES; dark brown, moist to wet, very stiff to very hard, iron oxide staining, ALLUVIUM Unit A			Sand backfill
20							298.0		
21						becoming gray			
22				PID = 500 PPM					
23		7							
24									
25		8A 8B	9-12-50/2" (50/2")	PID = 400 PPM		FAT CLAY (CH); mostly high plasticity FINES; few fine sand; dark red, very dense, ALLUVIUM Unit B	293.0		Bentonite
26									
27		9	15-50/2" (50/2")	PID = 300 PPM		becoming wet			
28		10	50/1" (50/1")	PID = 100 PPM					
29									
30		R-1A				CALCAREOUS LIMESTONE AND SANDSTONE, moderately weathered to highly weathered, dark brownish gray and light olive green, very fine grained to medium grained sand, strong to very strong, medium, 0° to 15° bedding angle, wet	288.0		
31									
32									Sand backfill
33		R-1B							
34						becoming vuggy			
35						LIMESTONE, freshly weathered, dark gray, wet, Comments go here	283.0		

Dataforensics

Borehole ID: BH-33

Client: Geo-Institute
Project Name: Vendor DIGGS Challenge
Project Number: 20250110 - DIGGS Challenge
Project Location: Somewhere Over the Rainbow
Date Started: Jun 04 2015 **Completed:** Jun 04 2015
Logged By: Scott Deaton **Checked By:**
Drilling Contractor: Big Dog Drillers
Northing: 1402115.2 **Easting:** 2272085.8 **Elevation:** 318.00
Drilling Method: 4.25" Hollow stem auger, NQ
Ground Water Levels
Equipment: CME 550, Arco 9000
At time of drilling 15.00 on Jun 04 2015
Hammer Type: Automatic
End of drilling 13.00 on Jun 04 2015
Notes: Notes go here
After drilling 15.00 on Jun 05 2015

Depth (ft)	Sample Type	Number	Blow Counts (N Value)	Environmental Data	Graphic	Material Description	Elevation (ft)	PID Concentration (125 250 375 500)	Well Details
37		R-2				LIMESTONE, freshly weathered, dark gray, wet, Comments go here			Concrete
38									
39									
40						Boring terminated at 40.0 feet.	278.0		
41									
42									
43									
44									
45							273.0		
46									
47									
48									
49									
50							268.0		
51									
52									
53									

Dataforensics

Borehole ID: BH-33

Client: Geo-Institute
Project Name: Vendor DIGGS Challenge
Project Number: 20250110 - DIGGS Challenge
Project Location: Somewhere Over the Rainbow
Date Started: Jun 04 2015 **Completed:** Jun 04 2015
Logged By: Scott Deaton **Checked By:**
Drilling Contractor: Big Dog Drillers
Northing: 1402115.2 **Easting:** 2272085.8 **Elevation:** 318.00
Drilling Method: 4.25" Hollow stem auger, NQ
Equipment: CME 550, Arco 9000
Hammer Type: Automatic
Notes: Notes go here

Ground Water Levels

At time of drilling	15.00 on Jun 04 2015
End of drilling	13.00 on Jun 04 2015
After drilling	15.00 on Jun 05 2015

Depth (ft)	Sample Type	Number	Blow Counts (N Value)	Environmental Data	Graphic	Material Description	Elevation (ft)	PID Concentration (125 250 375 500)	Well Details
						Asphalt			
1–3		1				POORLY GRADED GRAVEL WITH CLAY AND SAND (GP-GC); mostly fine to medium very hard subrounded flat GRAVEL; some fine hard well rounded elongated sand; few low plasticity fines; dark brownish black and light grayish brown, moist to wet, medium dense, stratified, trace ferrous nodules, trace construction debris, trace manganese, no odor, moderate cementation, iron oxide staining, max size = 3 in., Something else goes here, FILL Unit A			Concrete
4				PID = 100 PPM					
5							313.0		
7				PID = 200 PPM					
8–9		2	1-2-1 (3)			LEAN CLAY (CL); mostly low plasticity FINES no dilatancy; dark brown, moist, medium stiff to stiff, varved, FILL Unit A			Bentonite
10		3A	2-4-6 (10)	PID = 300 PPM			308.0		
11		3B				POORLY GRADED SAND (SP); mostly rounded SAND; light brown, moist, loose to medium dense, trace silt, hydrocarbon odor, ALLUVIUM Unit A			
12				PID = 400 PPM					
13–14		4	3-6-9 (15)						
15				PID = 500 PPM			303.0		
16		5	5-10-15 (25)			LEAN CLAY (CL); mostly medium plasticity FINES; dark brown, moist to wet, very stiff to very hard, iron oxide staining, ALLUVIUM Unit A			
17				PID = 600 PPM					

Dataforensics

Borehole ID: BH-33

Client: Geo-Institute
Project Name: Vendor DIGGS Challenge
Project Number: 20250110 - DIGGS Challenge
Project Location: Somewhere Over the Rainbow
Date Started: Jun 04 2015 **Completed:** Jun 04 2015
Logged By: Scott Deaton **Checked By:**
Drilling Contractor: Big Dog Drillers
Northing: 1402115.2 **Easting:** 2272085.8 **Elevation:** 318.00
Drilling Method: 4.25" Hollow stem auger, NQ
Equipment: CME 550, Arco 9000
Hammer Type: Automatic
Notes: Notes go here

Ground Water Levels
At time of drilling 15.00 on Jun 04 2015
End of drilling 13.00 on Jun 04 2015
After drilling 15.00 on Jun 05 2015

Depth (ft)	Sample Type	Number	Blow Counts (N Value)	Environmental Data	Graphic	Material Description	Elevation (ft)	PID Concentration (125 250 375 500)	Well Details
19		6	1-0-0 (WOH)			LEAN CLAY (CL); mostly medium plasticity FINES; dark brown, moist to wet, very stiff to very hard, iron oxide staining, ALLUVIUM Unit A			Sand backfill
20							298.0		
21						becoming gray			
22				PID = 500 PPM					
23		7							
24									
25		8A 8B	9-12-50/2" (50/2")	PID = 400 PPM		FAT CLAY (CH); mostly high plasticity FINES; few fine sand; dark red, very dense, ALLUVIUM Unit B	293.0		Bentonite
26									
27		9	15-50/2" (50/2")	PID = 300 PPM		becoming wet			
28		10	50/1" (50/1")	PID = 100 PPM					
29									
30		R-1A				CALCAREOUS LIMESTONE AND SANDSTONE, moderately weathered to highly weathered, dark brownish gray and light olive green, very fine grained to medium grained sand, strong to very strong, medium, 0° to 15° bedding angle, wet	288.0		
31									
32									Sand backfill
33		R-1B							
34						becoming vuggy			
35						LIMESTONE, freshly weathered, dark gray, wet, Comments go here	283.0		

Dataforensics

Borehole ID: BH-33

Client: Geo-Institute
Project Name: Vendor DIGGS Challenge
Project Number: 20250110 - DIGGS Challenge
Project Location: Somewhere Over the Rainbow
Date Started: Jun 04 2015 **Completed:** Jun 04 2015
Logged By: Scott Deaton **Checked By:**
Drilling Contractor: Big Dog Drillers
Northing: 1402115.2 **Easting:** 2272085.8 **Elevation:** 318.00
Drilling Method: 4.25" Hollow stem auger, NQ
Ground Water Levels
Equipment: CME 550, Arco 9000
At time of drilling 15.00 on Jun 04 2015
Hammer Type: Automatic
End of drilling 13.00 on Jun 04 2015
Notes: Notes go here
After drilling 15.00 on Jun 05 2015

Depth (ft)	Sample Type	Number	Blow Counts (N Value)	Environmental Data	Graphic	Material Description	Elevation (ft)	PID Concentration (125 250 375 500)	Well Details
37		R-2				LIMESTONE, freshly weathered, dark gray, wet, Comments go here			Concrete
38									
39									
40						Boring terminated at 40.0 feet.	278.0		
41									
42									
43									
44									
45							273.0		
46									
47									
48									
49									
50							268.0		
51									
52									
53									

Dataforensics

Borehole ID: BH-33

Client: Geo-Institute
Project Name: Vendor DIGGS Challenge
Project Number: 20250110 - DIGGS Challenge
Project Location: Somewhere Over the Rainbow
Date Started: Jun 04 2015 **Completed:** Jun 04 2015
Logged By: Scott Deaton **Checked By:**
Drilling Contractor: Big Dog Drillers
Northing: 1402115.2 **Easting:** 2272085.8 **Elevation:** 318.00
Drilling Method: 4.25" Hollow stem auger, NQ
Ground Water Levels
Equipment: CME 550, Arco 9000
At time of drilling 15.00 on Jun 04 2015
Hammer Type: Automatic
End of drilling 13.00 on Jun 04 2015
Notes: Notes go here
After drilling 15.00 on Jun 05 2015

Depth (ft)	Graphic	Material Description	Elevation (ft)	Sample Type	Number	Recovery % RQD	Blow Counts (N Value)	Moisture Content (%)	Liquid Limit (%)	Plastic Limit (%)	Fines Content (%)	Remarks
		Asphalt										
1		POORLY GRADED GRAVEL WITH CLAY AND SAND (GP-GC); mostly fine to medium very hard subrounded flat GRAVEL; some fine hard well rounded elongated sand; few low plasticity fines; dark brownish black and light grayish brown, moist to wet, medium dense, stratified, trace ferrous nodules, trace construction debris, trace manganese, no odor, moderate cementation, iron oxide staining, max size = 3 in., Something else goes here, FILL Unit A										
2					1			32			5	
3												
4												
5			313.0									
6		LEAN CLAY (CL); mostly low plasticity FINES no dilatancy; dark brown, moist, medium stiff to stiff, varved, FILL Unit A										
7												
8					2	100	1-2-1 (3)	33	41	11		
9												
10			308.0		3A	93	2-4-6 (10)	35			92	
11		POORLY GRADED SAND (SP); mostly rounded SAND; light brown, moist, loose to medium dense, trace silt, hydrocarbon odor, ALLUVIUM Unit A			3B							
12												
13					4	87	3-6-9 (15)	41			22	
14												
15			303.0									
16					5	67	5-10-15 (25)	39				
17		LEAN CLAY (CL); mostly medium plasticity FINES; dark brown, moist to wet, very stiff to very hard, iron oxide staining, ALLUVIUM Unit A										

Dataforensics

Borehole ID: BH-33

Client: Geo-Institute
Project Name: Vendor DIGGS Challenge
Project Number: 20250110 - DIGGS Challenge
Project Location: Somewhere Over the Rainbow
Date Started: Jun 04 2015 **Completed:** Jun 04 2015
Logged By: Scott Deaton **Checked By:**
Drilling Contractor: Big Dog Drillers
Northing: 1402115.2 **Easting:** 2272085.8 **Elevation:** 318.00
Drilling Method: 4.25" Hollow stem auger, NQ
Ground Water Levels
Equipment: CME 550, Arco 9000
At time of drilling 15.00 on Jun 04 2015
Hammer Type: Automatic
End of drilling 13.00 on Jun 04 2015
Notes: Notes go here
After drilling 15.00 on Jun 05 2015

Depth (ft)	Graphic	Material Description	Elevation (ft)	Sample Type	Number	Recovery % RQD	Blow Counts (N Value)	Moisture Content (%)	Liquid Limit (%)	Plastic Limit (%)	Fines Content (%)	Remarks
19		LEAN CLAY (CL); mostly medium plasticity FINES; dark brown, moist to wet, very stiff to very hard, iron oxide staining, ALLUVIUM Unit A			6	60	1-0-0 (WOH)	37	48,40	11,7	78	18.0 - 20.0 ft: Rough drilling
20		becoming gray	298.0									
23					7	100		44	48	17		
24												24.0 - 25.0 ft: Drill rods chattering
25		FAT CLAY (CH); mostly high plasticity FINES; few fine sand; dark red, very dense, ALLUVIUM Unit B	293.0		8A 8B	83	9-12-50/2" (50/2")	40	43	7		
26		becoming wet										
27					9	71	15-50/2" (50/2")	40	53	7		
28					10	100	50/1" (50/1")	43	55	16		
30		CALCAREOUS LIMESTONE AND SANDSTONE, moderately weathered to highly weathered, dark brownish gray and light olive green, very fine grained to medium grained sand, strong to very strong, medium, 0° to 15° bedding angle, wet	288.0		R-1A							
33		becoming vuggy			R-1B	100 60						
34		LIMESTONE, freshly weathered, dark gray, wet, Comments go here										
35			283.0									

Dataforensics

Borehole ID: BH-33

Client: Geo-Institute
Project Name: Vendor DIGGS Challenge
Project Number: 20250110 - DIGGS Challenge
Project Location: Somewhere Over the Rainbow
Date Started: Jun 04 2015 **Completed:** Jun 04 2015
Logged By: Scott Deaton **Checked By:**
Drilling Contractor: Big Dog Drillers
Northing: 1402115.2 **Easting:** 2272085.8 **Elevation:** 318.00
Drilling Method: 4.25" Hollow stem auger, NQ
Ground Water Levels
Equipment: CME 550, Arco 9000
At time of drilling 15.00 on Jun 04 2015
Hammer Type: Automatic
End of drilling 13.00 on Jun 04 2015
Notes: Notes go here
After drilling 15.00 on Jun 05 2015

Depth (ft)	Graphic	Material Description	Elevation (ft)	Sample Type	Number	Recovery % RQD	Blow Counts (N Value)	Moisture Content (%)	Liquid Limit (%)	Plastic Limit (%)	Fines Content (%)	Remarks
		LIMESTONE, freshly weathered, dark gray, wet, Comments go here			R-2	80 40						
37												
38												
39												
40		Boring terminated at 40.0 feet.	278.0									
41												
42												
43												
44												
45			273.0									
46												
47												
48												
49												
50			268.0									
51												
52												
53												
